


## 2007-09-27 Pbar Department Meeting

Thursday, September 27, 2007  
9:58 AM

- DVM noticed a strange feature of our skew quads SQ100 and SQ107. The coils are not set snugly into the laminations. This is a bad thing. DVM is talking with people in TD about how to fix this.

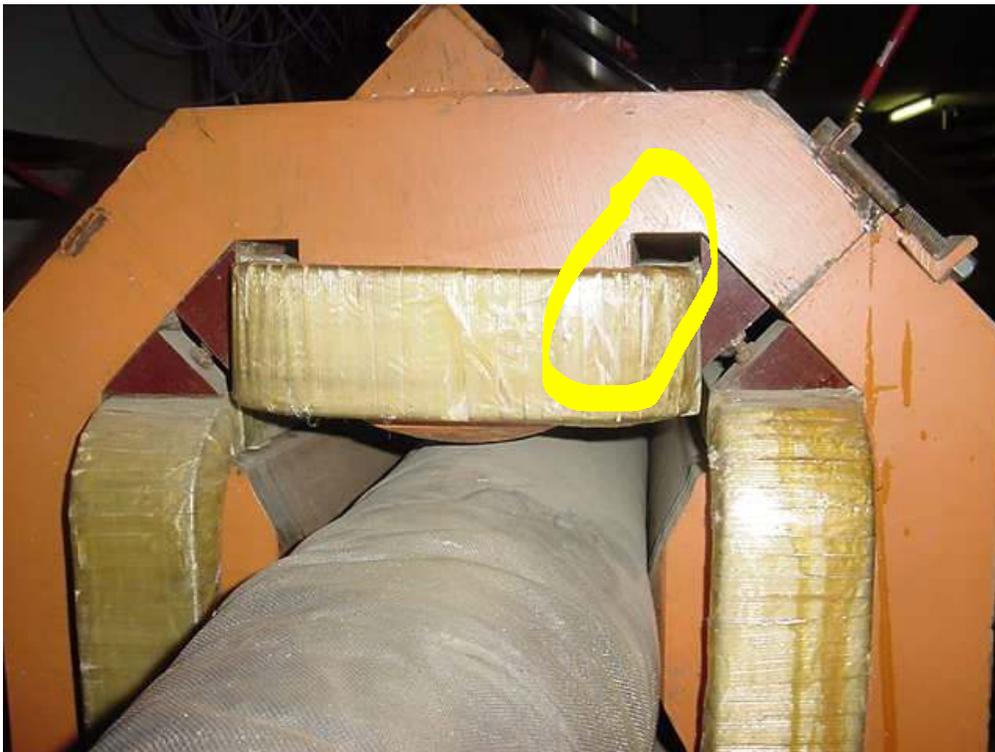

Pasted from <<http://www-bd.fnal.gov/cgi-mach/machlog.pl?nb=pbar07&action=view&page=-3667&button=yes>>

- Our new skew quad, SQ107, was delivered to AP0 this morning
- Leak on D:EKIK was fixed.



Pasted from <<http://www-bd.fnal.gov/cgi-mach/machlog.pl?nb=pbar07&action=view&page=-3673&button=yes>>

- Cryo filling.
- Target station
  - Elevator table in alcove failed, and was repaired.
- Power outage including emergency generator- scheduled for Monday - ES&H wants blocks on.
- Debuncher shunts moved, and water all hooked up.
- Accumulator BPM channels repaired - now out of spares.
  
- Machine Coordinator (7 people)
  - 1 vs 1.5 month
  - Part of on-call schedule?
- On-Call (9 people, actually 8 due to Machine Coordinator)
  - Expect on-call to spend hours in the MCR during the week.
  - Rotation
    - M&T, W&T, F, Sa, Su
    - 1 day
  - Scheduling
    - Make far in advance and people can trade as needed...
